ALAMANCE COUNTY LANDFILL
MONITORING WELLS
8-3-90

old	WELL DEPTHS new (current) — AS OF 6-21-91		
#6	#1	33 ft.	n.
#5	#2	30 ft.	
#4	#3	24 ft.	
#3 Abandoned April '91	#4	15 ft.	
Replacement well drilled 4-9-91	#4	51 ft	new well
#2	#5	19 ft.	
7-6-88 #7	#6	53 ft.	
#8	#7A	65 ft.	
#8	#7B	31½ ft.	
#9	#8A	65 ft.	
#9	#8B	26 ft.	
Drilled 4-8-91	#9	25 ft.	new well

*ALL 2" DIAMETER

**#7 and #8 Have shallow and deep wells
#4 is dry
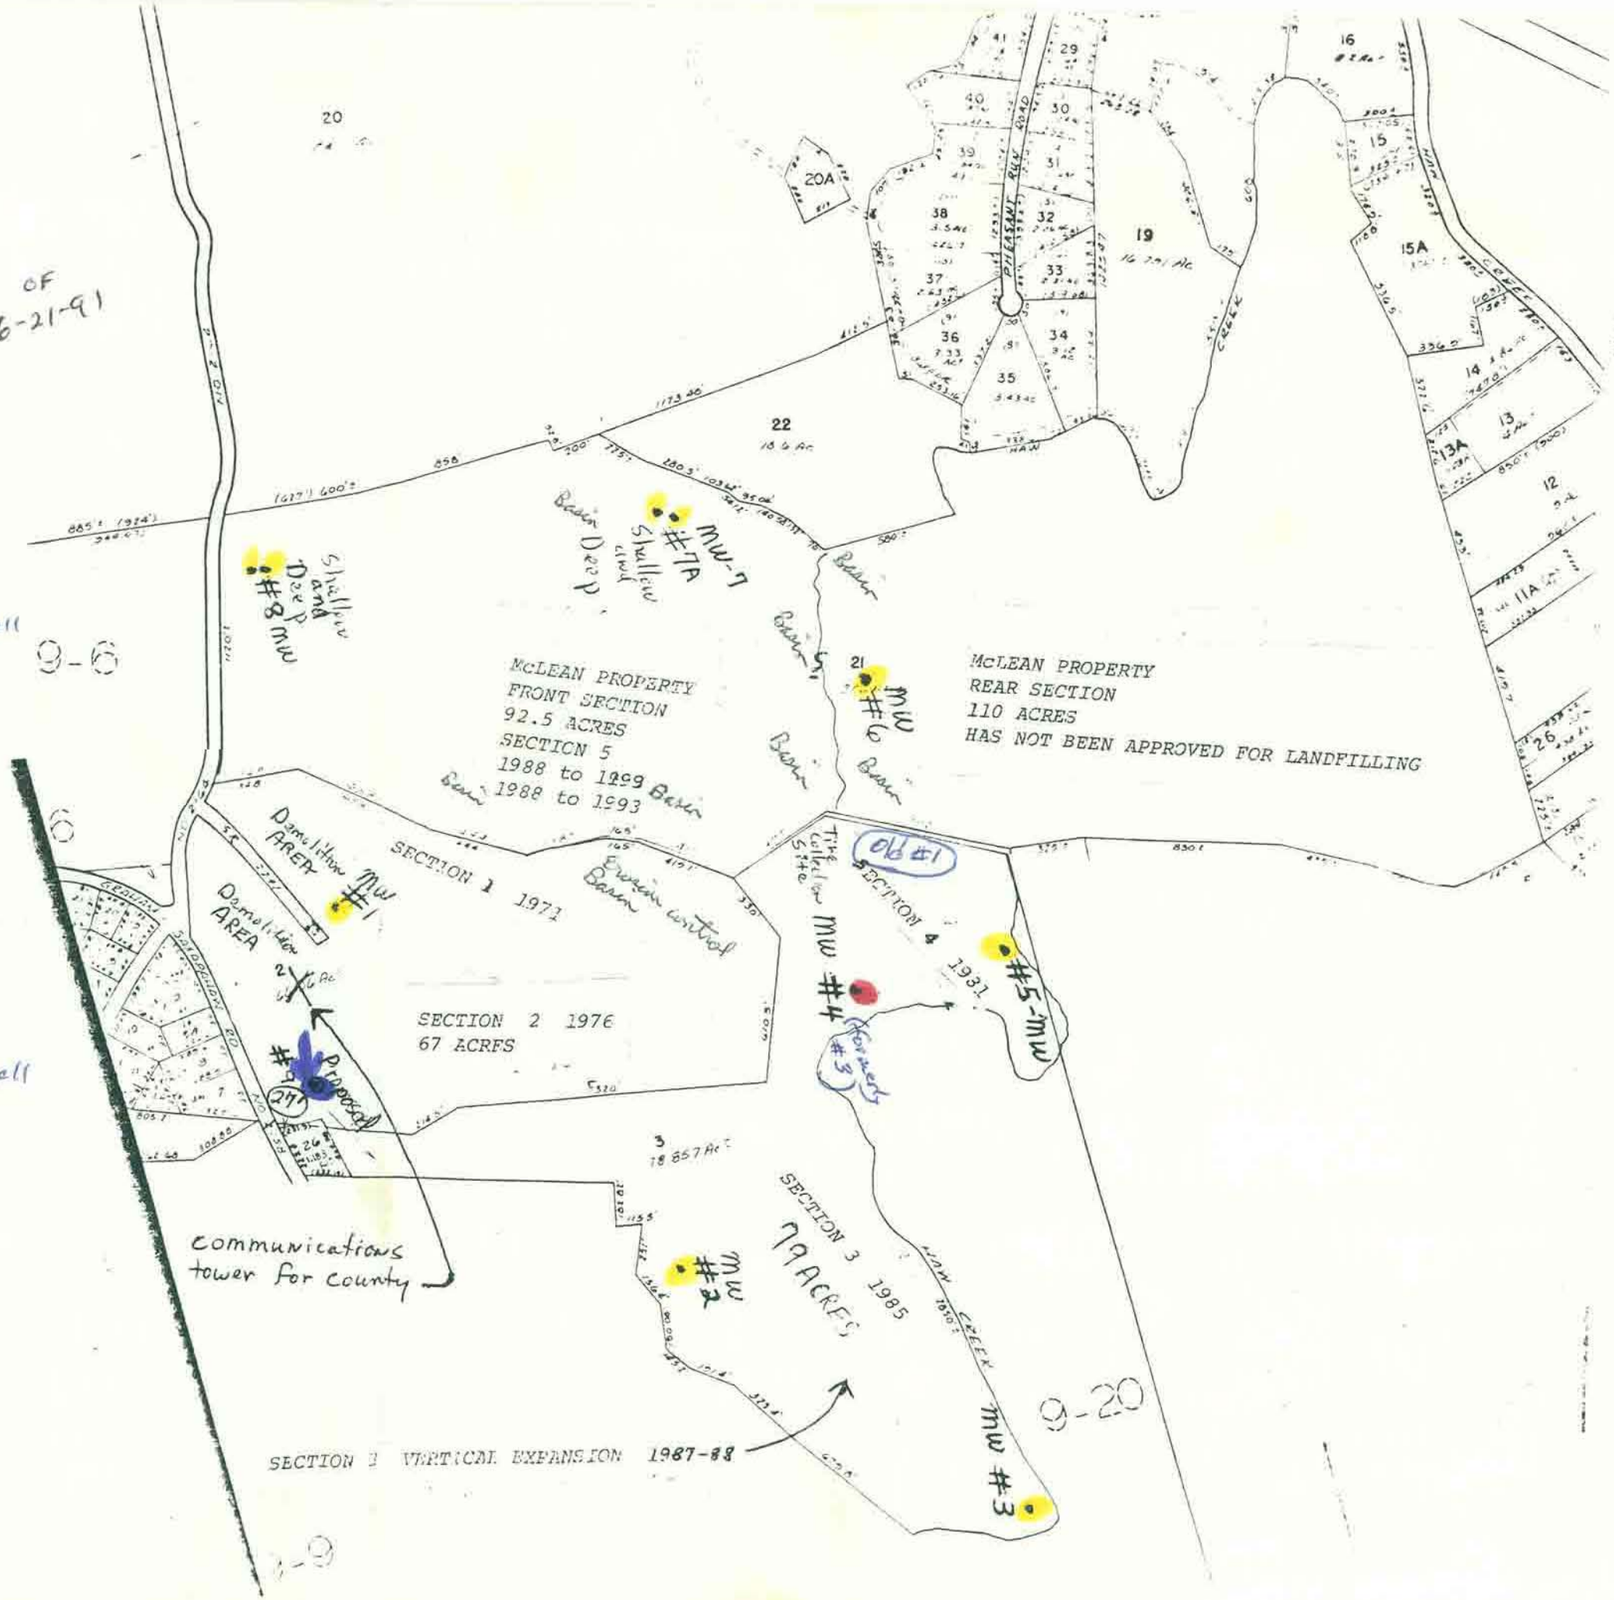
- old well #1 destroyed when drainage channel installed
